

ORIGINAL




**CIVIL ENGINEERING SERVICES FOR
CONTINUING SUPPLY**

MARCH 17, 2011

**LEON COUNTY BOARD OF
COUNTY COMMISSIONERS**

**1800-3 BLAIR STONE ROAD
TALLAHASSEE, FL 32308**

***Bill Proctor, District 1
Jane G. Saules, District 2
John E. Dailey, District 3
Bryan Desloge, District 4
Kristin Dozier, District 5
Nick Maddox, At-Large
Akin Akinyemi, At-Large***

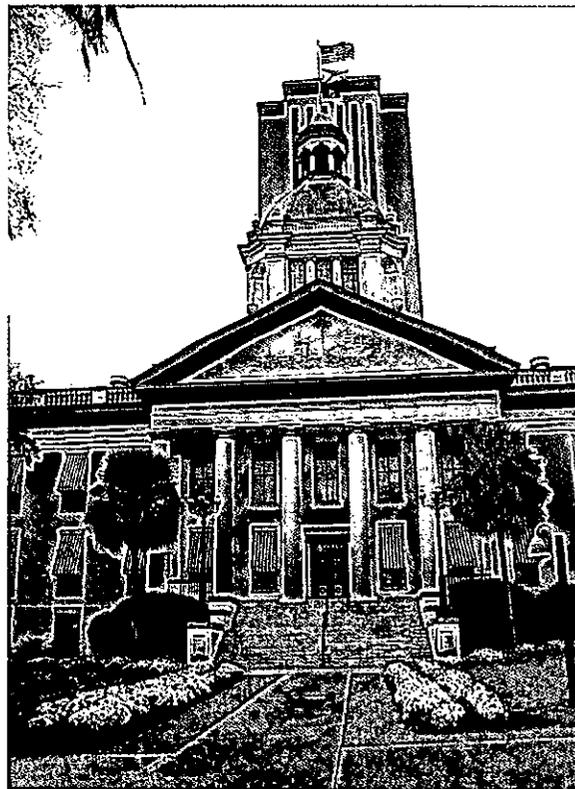

PREPARED BY:



PREBLE-RISH INC
CONSULTING ENGINEERS & SURVEYORS

**36 Jasper Thomas Road
Crawfordville, FL 32327
850.528.0300**

Quincy, FL

Monticello, FL

Panama City, FL

Port St. Joe, FL

Santa Rosa Beach, FL

Blountstown, FL

Ft. Walton Beach, FL

Suwannee, FL

Daphne, AL



PREBLE-RISH INC

CONSULTING ENGINEERS & SURVEYORS

March 17, 2011 (2pm ET)

Via Hand Delivery

Leon County Board of County Commissioners
Purchasing Division
1800-3 Blair Stone Road
Tallahassee, FL 32308

RE: **Leon County
Civil Engineering Services for Continuing Supply**

Dear Leon County Board of County Commissioners:

Preble-Rish, Inc. (PRI) is pleased to have the opportunity to offer professional engineering services to Leon County.



As you will see in our submittal, our firm is a full-service organization with dedicated professionals utilizing the latest engineering technology to provide quality products and services for our governmental clients. PRI's primary office for this contract is located only nine (9) miles away from Leon County at 36 Jasper Thomas Road, Crawfordville FL, 32327, please see attached map.


In this statement of qualifications, we will demonstrate that our team is the best-suited to be the County's Engineer for a number of reasons. Not only do we have the experience and expertise needed, but we are committed professionally and understand County/City/Municipal Government and their needs. In addition, we are one of the few organizations primarily dedicated to serving the public sector. Preble-Rish, Inc. has completed a wide variety of engineering projects which have vastly improved the landscape and infrastructure of Counties and Cities throughout Northwest Florida. PRI has had the opportunity to work on several projects in Leon County in the last 12 months.

PRI is the general consulting engineer for Wakulla, Gadsden, and also Jefferson County. We feel it is important to note that we also have offices in all three Florida Counties that border Leon County. For over 19 years, we have served up to 50 government/utility entities. Our dedication to our clients can be proven by the fact that we have not lost a single government client once we began working for them. This experience in turn provides us a clear understanding of your needs making Preble-Rish Inc., the "team of choice."

Preble-Rish Inc. has always given back generously to the communities in which we work and we would welcome any occasion to strengthen our corporate citizenship with Leon County.

Again we appreciate the opportunity to submit our qualifications and look forward to building a relationship with Leon County.

Sincerely,
PREBLE-RISH, INC.


Alan Wise, P.E.
Project Manager

Submitted: 1 Original & 3 Copies

cc Mr. Ralph Rish, President, PRI
Mr. Chris Forehand, P.E., Vice-President, C.O.O., PRI
Mr. Warren Yeager, Business Development Manager, PRI

Port St. Joe

324 Marina Drive
Port St. Joe, FL 32456
P 850.227.7200
F 850.227.7215

Panama City

203 Aberdeen Parkway
Panama City, FL 32405
P 850.522.0644
F 850.522.1011

Santa Rosa Beach

877 CR 393 North
Santa Rosa Beach, FL 32459
P 850.267.0759
F 866.557.0076

Bristol

10490 NW Main Street
Bristol, FL 32321
P 850.643.2771
F 850.643.2910

Quincy

20 East Washington Street
Quincy, FL 32351
P 850.875.4751

Blountstown

20684 Central Avenue East
Blountstown, FL 32424
P 850.674.3300
F 850.674.3330

Crawfordville

36 Jasper Thomas Road
Crawfordville, FL 32327
P 850.274.9866

Monticello

Gadsden Square
187 East Walnut Street
Monticello, FL 32344
P 850.997.2175



PREBLE-RISH INC
CONSULTING ENGINEERS & SURVEYORS

**CONTINUING SUPPLY
TABLE OF CONTENTS**

- A. CONTRACTOR INFORMATION**
- B. EXECUTIVE SUMMARY**
- C. REQUIRED FORMS**

Specific Proposal Information for Each Work Category

a. STORMWATER ENGINEERING

- A. ABILITY OF PROFESSIONAL PERSONNEL
- B. EXPERIENCE WITH PROJECTS OF A SIMILAR TYPE AND SIZE
- C. WILLINGNESS TO MEET SCHEDULE AND BUDGET REQUIRMENTS
- D. EFFECT OF FIRM'S RECENT, CURRENT, AND PROJECTED WORKLOAD
- E. EFFECT OF PROJECT TEAM LOCATION
- F. APPROACH TO PROJECT

b. ROADWAY DESIGN

- A. ABILITY OF PROFESSIONAL PERSONNEL
- B. EXPERIENCE WITH PROJECTS OF A SIMILAR TYPE AND SIZE
- C. WILLINGNESS TO MEET SCHEDULE AND BUDGET REQUIRMENTS
- D. EFFECT OF FIRM'S RECENT, CURRENT, AND PROJECTED WORKLOAD
- E. EFFECT OF PROJECT TEAM LOCATION
- F. APPROACH TO PROJECT

d. STRUCTURAL ENGINEERING

- A. ABILITY OF PROFESSIONAL PERSONNEL
- B. EXPERIENCE WITH PROJECTS OF A SIMILAR TYPE AND SIZE
- C. WILLINGNESS TO MEET SCHEDULE AND BUDGET REQUIRMENTS
- D. EFFECT OF FIRM'S RECENT, CURRENT, AND PROJECTED WORKLOAD
- E. EFFECT OF PROJECT TEAM LOCATION
- F. APPROACH TO PROJECT

g. CONSTRUCTION ENGINEERING AND INSPECTION SERVICES

- A. ABILITY OF PROFESSIONAL PERSONNEL
- B. EXPERIENCE WITH PROJECTS OF A SIMILAR TYPE AND SIZE
- C. WILLINGNESS TO MEET SCHEDULE AND BUDGET REQUIRMENTS
- D. EFFECT OF FIRM'S RECENT, CURRENT, AND PROJECTED WORKLOAD
- E. EFFECT OF PROJECT TEAM LOCATION
- F. APPROACH TO PROJECT

TABLE OF CONTENTS PAGE 2

h. SURVEYING

- A. ABILITY OF PROFESSIONAL PERSONNEL
- B. EXPERIENCE WITH PROJECTS OF A SIMILAR TYPE AND SIZE
- C. WILLINGNESS TO MEET SCHEDULE AND BUDGET REQUIRMENTS
- D. EFFECT OF FIRM'S RECENT, CURRENT, AND PROJECTED WORKLOAD
- E. EFFECT OF PROJECT TEAM LOCATION
- F. APPROACH TO PROJECT

i. SUBDIVISION AND SITE DEVELOPMENT ENGINEERING

- A. ABILITY OF PROFESSIONAL PERSONNEL
- B. EXPERIENCE WITH PROJECTS OF A SIMILAR TYPE AND SIZE
- C. WILLINGNESS TO MEET SCHEDULE AND BUDGET REQUIRMENTS
- D. EFFECT OF FIRM'S RECENT, CURRENT, AND PROJECTED WORKLOAD
- E. EFFECT OF PROJECT TEAM LOCATION
- F. APPROACH TO PROJECT

j. PARKS AND RECREATIONAL FACILITY ENGINEERING

- A. ABILITY OF PROFESSIONAL PERSONNEL
- B. EXPERIENCE WITH PROJECTS OF A SIMILAR TYPE AND SIZE
- C. WILLINGNESS TO MEET SCHEDULE AND BUDGET REQUIRMENTS
- E. EFFECT OF FIRM'S RECENT, CURRENT, AND PROJECTED WORKLOAD
- F. EFFECT OF PROJECT TEAM LOCATION
- G. APPROACH TO PROJECT

k. UTILITY ENGINEERING

- A. ABILITY OF PROFESSIONAL PERSONNEL
- B. EXPERIENCE WITH PROJECTS OF A SIMILAR TYPE AND SIZE
- C. WILLINGNESS TO MEET SCHEDULE AND BUDGET REQUIRMENTS
- D. EFFECT OF FIRM'S RECENT, CURRENT, AND PROJECTED WORKLOAD
- E. EFFECT OF PROJECT TEAM LOCATION
- F. APPROACH TO PROJECT



PREBLE-RISH INC
CONSULTING ENGINEERS & SURVEYORS

A. CONTRACTOR INFORMATION



PREBLE-RISH INC
CONSULTING ENGINEERS & SURVEYORS

OFFICE LOCATION PERFORMING THE WORK

Preble-Rish, Inc. (PRI) has offices in Port St. Joe, Panama City, Santa Rosa Beach, Quincy, Blountstown, Crawfordville, Monticello, Suwannee, Ft. Walton Beach, and just recently added a new office in Daphne, Alabama. Our wide-area network allows us to efficiently utilize the services of our professional staff from any office, on any job, while managing the project from its nearest and most logical location.

Preble-Rish, Inc. has a **Crawfordville office** that is currently located near you, and is ready to serve as the production office for Leon County. We propose to dedicate Mr. Alan Wise, a Professional Engineer who lives in Leon County, as the Project Manager for Leon County. Our Crawfordville office is approximately 19 miles from the Leon County Courthouse. We are confident in his ability to serve your professional needs with ease. He will have access to all of the expert staff within the entire firm as well as the staff in his office locally. In addition, Mr. Chris Forehand, from our Panama City office, will serve in a quality assurance/Quality Control Role to Mr. Wise.



PREBLE-RISH, INC.
MR. ALAN WISE
36 Jasper Thomas Road
Crawfordville, FL 32327
P 850.274.9866
wisea@preble-rish.com

PREBLE-RISH, INC.
MR. CHRIS FOREHAND
203 Aberdeen Parkway
Panama City, FL 32405
P 850.522.0644
forehanc@preble-rish.com



PREBLE-RISH INC
CONSULTING ENGINEERS & SURVEYORS

B. EXECUTIVE SUMMARY

EXECUTIVE SUMMARY

Preble-Rish, Inc. (PRI) is a professional engineering and surveying firm, established in 1991. From its first office in Port St. Joe, the firm has expanded across Florida and currently is one of the most widely known and respected firms in the area. PRI is a full-service consulting engineering and surveying firm helping public and private clients improve the environment and infrastructure. For over 19 years, we have been providing innovative solutions developed through strong client relationships of mutual trust and respect and a commitment to quality and integrity.

PRI serves a client base focused on governmental and municipal agencies including the Counties of... Bay, Calhoun, Franklin, Gadsden, Gulf, Jackson, Jefferson, Liberty, Okaloosa, Wakulla, Walton, Washington, the Cities of... Apalachicola, Blountstown, Bristol, Callaway, Chattahoochee, DeFuniak Springs, Freeport, Gretna, Lynn Haven, Marianna, Midway, Mexico Beach, Panama City Beach, Parker, Port St. Joe, Wewahitchka, Baldwin County AL, The City of Gulf Shores, the Towns of... Altha, Campbellton, Paxton, and Wausau.

Other Governmental clients include... Florida Department of Transportation (FDOT), Northwest Florida Transportation Corridor Authority, Northwest Florida Water Management District (NFWMD), and the Port St Joe Port Authority.

Utility clients include... Gulf Coast Electric Cooperative (GCEC), Lighthouse Utilities Company, Progress Energy, Regional Utilities of South Walton County, TECO Peoples Gas, and AT&T (Bell South).

Clients that are School Systems include... Bay District Schools, Gulf County School District, Baldwin County Schools, and Leon County Schools.

Our extensive client base requires PRI to provide a variety of services, fulfilling the diverse needs of Northwest Florida.

From the original three-person firm, PRI has grown to 87 employees at present. Our creativity and willingness to take on new challenges, coupled with our casual, but hard-working culture, makes us perfectly adapted to the type of work required by the clients we serve. Our mission is to provide our clients with a cost efficient, precise product that PRI can be proud to endorse.

Mr. Alan Wise, will be the contact for Leon County. He is a Project Manager and is authorized to make representations for PRI. His office is located at 36 Jasper Thomas Road, Crawfordville, FL 32327. The office number is 850.528.0300. He can also be reached via e-mail @ wisea@preble-rish.com.

We take pride in the fact that the firm continues to be re-hired for ongoing contracts with governmental clients.

Quality Control

PRI believes quality is the most important part of any business and this attribute alone leads to the completion of a successful project. Our company's strategy for maintaining the cost and quality control that our clients deserve relies not only on our experience in design, but also our trained staff of quality control review personnel.



Engineering Services

Preble-Rish, Inc. currently has a staff of 12 Professional Engineers. PRI is committed to providing professional engineering services as follows:

- Construction Oversight
- Design / Build
- Development of Regional Impact Studies (DRI's)
- Drainage and Flood Evaluations
- FEMA Map Revisions
- Landfills
- Mapping
- Marinas
- Master Planned Communities
- Mining Projects
- Planning
- Production Wells
- Residential, Commercial and Industrial Developments
- Reuse
- Roads and Bridges
- Signalization Design
- Small Scale Comprehensive Plan Amendments
- Large Scale Comprehensive Plan Amendments
- Stormwater Design
- System Evaluations
- Traffic Studies
- Transportation Studies / Investigations
- Wastewater Collection Systems
- Wastewater Treatment Plants
- Water Distribution Systems
- Water Plants


Permitting Services

PRI is experienced in providing professional permitting services as follows:

- County and City Right-of-Way Use
- FDEP Beaches & Shores
- FDEP Dredge & Fill
- FDEP Solid Waste
- FDEP Water and Wastewater
- FDOT Connection
- FDOT Drainage
- FDOT Utility Use
- HRS Commercial Septic System
- Local Government Development Approval
- NFWMD - Consumptive Use
- NFWMD - ERP (Environmental Resource Permitting)
- Stormwater
- U.S. Coast Guard Bridge
- USACE Dredge & Fill

Surveying Services

Below is a list of our broad range of services and expertise in the areas of surveying:

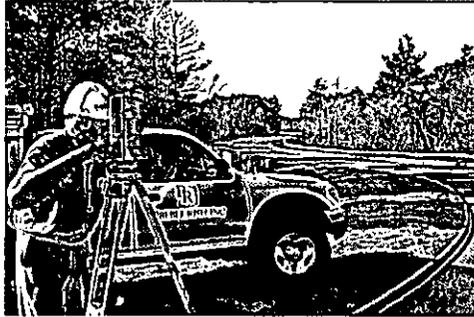

Accident/Forensic Surveys
ALTA Surveys
As-Built Surveys
Baseline Control
Hydro-graphic Bathymetric
Subaqueous Surveying & Mapping
Building Setbacks
Boundary Survey
Centerline Staking
Condominium Docs
Construction/Reconstruction
Construction Stakeout
Control Surveys
Court Exhibits
Cross-Sections
Drainage Surveys
Easement Surveys
Foundation Surveys
GPS
Horizontal Control
Land Area Computations
Legal Descriptions
Mitigation Site Surveys
Municipal Plat Review
Preliminary, Final, and Re-Plat Surveys
Roadway Layout
Route Surveys
Sectional Survey
Sketch of Description
Subdivision Boundaries
Submerged Land Lease
Topographic Surveys
Utility Layout
Utility Location Surveys
Vertical Control
Wetland Location (Conventional/Submeter)

Preble-Rish, Inc. currently has a staff of 3 Professional Land Surveyors and 5 Field Crews.

Grant/Loan Assistance

Preble-Rish, Inc. is well versed in State and Federal grant/loan programs. We are perfectly equipped to offer assistance to all municipal and County governments in this endeavor as well as with Community Budget Issue requests.

The following is a list of programs PRI has experience with:

- Florida Department of Environmental Protection-State Revolving Funds (FDEP-SRF)
- Bond Issue Requirements
- Community Budget Issue Requests (CBIR) - State Legislature
- Community Development Block Grants (CDBG)
- Florida Department of Transportation (FDOT) Small County Road Assistance Programs (SCRAPs)

- Florida Department of Transportation (FDOT) Small County Outreach Program (SCOPs)
- Florida Department of Transportation (FDOT) Trip Funds
- Florida Recreation Development Assistance Program (FRDAP)
- Northwest Florida Water Management District (NFWFMD) - Grant Programs
- United States Department of Agriculture (USDA) - Rural Development

Construction Administration & Inspection Services

Preble-Rish, Inc. offers construction administration and inspection to compliment a wide range of projects. Our experienced staff can keep any job running smoothly. We feel that on-site inspection is a vital part of all projects. PRI currently has 12 qualified Inspectors on staff to provide our clients with inspection services. PRI also reviews pay requests, attends progress meetings with the client and the contractor, as well as certifies the project once construction is complete.

Memberships

- American Society of Civil Engineers (ASCE)
- American Water Works Association (AWWA) - Florida
- American Water Works Association(AWWA) - National
- Florida Engineering Society (FES)
- Florida Water Environment Association (FWEA)
- Institute of Transportation Engineers (ITE)
- Society of American Military Engineers (SAME)
- Water Environment Federation (WEF)

FDOT Certifications

Group 3 – Highway Design – Roadway

- 3.1 – Minor Highway Design
- 3.2 – Major Highway Design

Group 4 – Highway Design – Bridges

- 4.1.1 – Miscellaneous Structures
- 4.1.2 – Minor Bridge Design

Group 7 – Traffic Operations Design

- 7.1- Signing, Pavement Marking and Channelization

Group 8 – Surveying and Mapping

- 8.1 – Control Surveying
- 8.2 – Design, Right of Way & Construction Surveying
- 8.4 – Right of Way Mapping

Group 10 – Construction Engineering Inspection

- 10.1 – Roadway Construction Engineering Inspection

Group 13 – Planning

- 13.5 – Subarea/Corridor Planning
- 13.6 – Land Planning/Engineering

Licenses

Florida Board of Professional Engineers - License No. 6155

Florida Board of Professional Surveyors & Mappers
License No. LB7137

Declaration

This RFP is in all respects fair and in good faith without collusion or fraud and the signer of this RFP has the authority to bind principal proponent.



PREBLE-RISH INC
CONSULTING ENGINEERS & SURVEYORS

C. REQUIRED FORMS

RFP Title: Request for Proposals for Civil Engineering Services, Continuing Supply
Proposal Number: BC-03-17-11-25
Opening Date: Thursday, March 17, 2011 at 2:00 PM

PROPOSAL RESPONSE COVER SHEET


THIS PAGE IS TO BE COMPLETED AND INCLUDED AS THE COVER SHEET FOR YOUR RESPONSE TO THE REQUEST FOR PROPOSALS.

The Board of County Commissioners, Leon County, reserves the right to accept or reject any and/or all bids in the best interest of Leon County.

Keith M. Roberts, Purchasing Director

John Dailey, Chairman
Leon County Board of County Commissioners

This bid response is submitted by the below named firm/individual by the undersigned authorized representative.

BY Preble-Rish, Inc.
(Firm Name) 
(Authorized Representative)
Alan Wise
(Printed or Typed Name)
ADDRESS 36 Jasper Thomas Road
CITY, STATE, ZIP Crawfordville, FL 32327
TELEPHONE 850-528-0300
FAX 850-522-1011

ADDENDA ACKNOWLEDGMENTS: (IF APPLICABLE)

Addendum #1 dated 03/03/11 Initials AW Addendum #3 dated _____ Initials _____
Addendum #2 dated _____ Initials _____ Addendum #4 dated _____ Initials _____

PLEASE MARK WHICH CATEGORIES FOR WHICH YOU WISH TO BE CONSIDERED:

- | | |
|---|---|
| <input checked="" type="checkbox"/> a. Stormwater Engineering | <input checked="" type="checkbox"/> h. Surveying |
| <input checked="" type="checkbox"/> b. Roadway Design | <input checked="" type="checkbox"/> i. Subdivision and Site Development Engineering |
| <input type="checkbox"/> c. Traffic and Intersection Engineering | <input checked="" type="checkbox"/> j. Parks and Recreational Facility Engineering |
| <input checked="" type="checkbox"/> d. Structural Engineering | <input checked="" type="checkbox"/> k. Utility Engineering |
| <input checked="" type="checkbox"/> e. Geotechnical Services | |
| <input type="checkbox"/> f. Environmental Support Services | |
| <input checked="" type="checkbox"/> g. Construction Engineering and Inspection Services | |

RFP Title: Request for Proposals for Civil Engineering Services, Continuing Supply
Proposal Number: BC-03-17-11-25
Opening Date: Thursday, March 17, 2011 at 2:00 PM


AFFIDAVIT CERTIFICATION
IMMIGRATION LAWS

Leon County will not intentionally award County contracts to any contractor who knowingly employs unauthorized alien workers, constituting a violation of the employment provisions contained in 8 U.S.C. Section 1324 A(e) (Section 274a(e) of the Immigration and Nationality Act ("INA")).

Leon County may consider the employment by any Contractor of Unauthorized Aliens a violation of Section 274A(e) of the INA. Such violation by the Recipient of the employment provision contained in Section 274A(e) of the INA shall be ground for unilateral cancellation of the contract by Leon County.

BIDDER ATTESTS THAT THEY ARE FULLY COMPLIANT WITH ALL APPLICABLE IMMIGRATION LAWS (SPECIFICALLY TO THE 1986 IMMIGRATION ACT AND SUBSEQUENT AMENDMENTS).

Company Name: PrebleRish, Inc.

Signature:  Title: Project Manager
Alan Wise

STATE OF Florida
COUNTY OF Bay

Sworn to and subscribed before me this 16 day of March, 2011.

Personally known X


NOTARY PUBLIC

OR Produced identification _____

Notary Public - State of Florida

(Type of identification)

My commission expires: Aug 16, 2013

Amber Leigh Fowler
Printed, typed, or stamped
commissioned name of notary public

The signee of this Affidavit guarantees, as evidenced by the sworn affidavit required herein, the truth and accuracy of this affidavit to interrogatories hereinafter made.

**LEON COUNTY RESERVES THE RIGHT TO REQUEST SUPPORTING DOCUMENTATION,
AS EVIDENCE OF SERVICES PROVIDED, AT ANY TIME.**



RFP Title: Request for Proposals for Civil Engineering Services, Continuing Supply
Proposal Number: BC-03-17-11-25
Opening Date: Thursday, March 17, 2011 at 2:00 PM

EQUAL OPPORTUNITY/AFFIRMATIVE ACTION STATEMENT

1. The contractors and all subcontractors hereby agree to a commitment to the principles and practices of equal opportunity in employment and to comply with the letter and spirit of federal, state, and local laws and regulations prohibiting discrimination based on race, color, religion, national region, sex, age, handicap, marital status, and political affiliation or belief.
2. The contractor agrees to comply with Executive Order 11246, as amended, and to comply with specific affirmative action obligations contained therein.

Signed:



Alan Wise

Title:

Project Manager

Firm:

Preble-Rish, Inc.

RFP Title: Request for Proposals for Civil Engineering Services, Continuing Supply
Proposal Number: BC-03-17-11-25
Opening Date: Thursday, March 17, 2011 at 2:00 PM

INSURANCE CERTIFICATION FORM

To indicate that Bidder/Respondent understands and is able to comply with the required insurance, as stated in the bid/RFP document, Bidder/Respondent shall submit this insurances sign-off form, signed by the company Risk Manager or authorized manager with risk authority.

A. Is/are the insurer(s) to be used for all required insurance (except Workers' Compensation) listed by Best with a rating of no less than A:VII?

YES NO

Commercial General Liability:	Indicate Best Rating: Indicate Best Financial Classification:	<u> A+ </u> <u> XV </u>
Business Auto:	Indicate Best Rating: Indicate Best Financial Classification:	<u> A+ </u> <u> XV </u>
Professional Liability:	Indicate Best Rating: Indicate Best Financial Classification:	<u> A+ </u> <u> XV </u>

1. Is the insurer to be used for Workers' Compensation insurance listed by Best with a rating of no less than A:VII?

YES NO

Indicate Best Rating: A
Indicate Best Financial Classification: XV

If answer is NO, provide name and address of insurer:

2. Is the Respondent able to obtain insurance in the following limits (next page) for this professional services agreement?

YES NO

Insurance will be placed with Florida admitted insurers unless otherwise accepted by Leon County. Insurers will have A.M. Best ratings of no less than A:VII unless otherwise accepted by Leon County.

Required Coverage and Limits

The required types and limits of coverage for this bid/request for proposals are contained within the solicitation package. Be sure to carefully review and ascertain that bidder/proposer either has coverage or will place coverage at these or higher levels.

RFP Title: Request for Proposals for Civil Engineering Services, Continuing Supply
Proposal Number: BC-03-17-11-25
Opening Date: Thursday, March 17, 2011 at 2:00 PM

Required Policy Endorsements and Documentation

Certificate of Insurance will be provided evidencing placement of each insurance policy responding to requirements of the contract.

Deductibles and Self-Insured Retentions

Any deductibles or self-insured retentions must be declared to and approved by the County. At the option of the County, either: the insurer shall reduce or eliminate such deductibles or self-insured retentions as respects the County, its officers, officials, employees and volunteers; or the Contractor shall procure a bond guaranteeing payment of losses and related investigations, claim administration and defense expenses.

Endorsements to insurance policies will be provided as follows:

Additional insured (Leon County, Florida, its Officers, employees and volunteers) -
General Liability & Automobile Liability

Primary and not contributing coverage-
General Liability & Automobile Liability

Waiver of Subrogation (Leon County, Florida, its officers, employees and volunteers)- General
Liability, Automobile Liability, Workers' Compensation and Employer's Liability

Thirty days advance written notice of cancellation to County - General Liability,
Automobile Liability, Worker's Compensation & Employer's Liability.

Professional Liability Policy Declaration sheet as well as claims procedures for each applicable policy to be provided


Please mark the appropriate box:

Coverage is in place

Coverage will be placed, without exception

The undersigned declares under penalty of perjury that all of the above insurer information is true and correct.

Name Alan Wise
Typed or Printed

Signature 

Date 3/16/11

Title Project Manager
(Company Risk Manager or Manager with Risk

Authority)

RFP Title: Request for Proposals for Civil Engineering Services, Continuing Supply
Proposal Number: BC-03-17-11-25
Opening Date: Thursday, March 17, 2011 at 2:00 PM

**CERTIFICATION REGARDING DEBARMENT, SUSPENSION,
And OTHER RESPONSIBILITY MATTERS
PRIMARY COVERED TRANSACTIONS**

1. The prospective primary participant certifies to the best of its knowledge and belief, that it and its principals:
 - a) Are not presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded from covered transactions by any Federal department or agency;
 - b) Have not within a three-year period preceding this been convicted of or had a civil judgement rendered against them for commission of fraud or a criminal offense in connection with obtaining, attempting to obtain, or performing a public (Federal, State or local) transaction or contract under a public transaction; violation of Federal or State antitrust statutes or commission of embezzlement, theft, forgery, bribery, falsification or destruction of records, making false statements, or receiving stolen property;
 - c) Are not presently indicted for or otherwise criminally or civilly charged by a governmental entity (Federal, State or local) with commission of any of these offenses enumerated in paragraph (1)(b) of this certification; and
 - d) Have not within a three-year period preceding this application/proposal had one or more public transactions (Federal, State or local) terminated for cause or default.
2. Where the prospective primary participant is unable to certify to any of the statements in this certification, such prospective participant shall attach an explanation to this proposal.
3. No subcontract will be issued for this project to any party which is debarred or suspended from eligibility to receive federally funded contracts.



Signature

Project Manager

Title

Preble-Rish, Inc.

Contractor/Firm

36 Jasper Thomas Road, Crawfordville, FL 32327

Address

LOCAL VENDOR CERTIFICATION

The undersigned, as a duly authorized representative of the vendor listed herein, certifies to the best of his/her knowledge and belief, that the vendor meets the definition of a "Local Business." For purposes of this section, "local business" shall mean a business which:

- a) Has had a fixed office or distribution point located in and having a street address within Leon, Gadsden, Wakulla, or Jefferson County for at least six (6) months immediately prior to the issuance of the request for competitive bids or request for proposals by the County; and
- b) Holds any business license required by Leon County (or one of the other local counties), and, if applicable, the City of Tallahassee; and
- c) Is the principal offeror who is a single offeror; a business which is the prime contractor and not a subcontractor; or a partner or joint venturer submitting an offer in conjunction with other businesses.

Please complete the following in support of the self-certification and submit copies of your County and City business licenses. Failure to provide the information requested will result in denial of certification as a local business.

Business Name: Preble-Rish, Inc.	
Current Local Address: 36 Jasper Thomas Road Crawfordville, FL 32327	Phone: 850-528-0300 Fax: 850-522-1011
If the above address has been for less than six months, please provide the prior address.	
Length of time at this address:	
Home Office Address: 324 Marina Drive Port St. Joe, FL 32456	Phone: 850-227-7200 Fax: 850-227-7215

Signature of Authorized Representative

3/16/11

Date

STATE OF Florida
COUNTY OF Bay

The foregoing instrument was acknowledged before me this 16 day of March, 2011.

By Alan Wise of Preble-Rish, Inc.
(Name of officer or agent, title of officer or agent) (Name of corporation acknowledging)

a Florida corporation, on behalf of the corporation. He/she is personally known to me
(State or place of incorporation)

or has produced _____ as identification.
(type of identification)

Amber Leigh Fowler
Signature of Notary
Amber Leigh Fowler
Print, Type or Stamp Name of Notary
Administrative Assistant
Title or Rank

Return Completed form with supporting documents to:

Leon County Purchasing Division
1800-3 Blair Stone Road
Tallahassee, Florida 32308



Serial Number, If Any



Leon County

Board of County Commissioners

301 South Monroe Street, Tallahassee, Florida 32301
(850) 606-5302 www.leoncountyfl.gov

Purchasing Division
1800-3 Blair Stone Road
(corner of Miccosukee and Blair Stone Roads)
Tallahassee, Florida 32308
(850) 606-1600

Commissioners

BILL PROCTOR
District 1

JANE G. SAULS
District 2

JOHN DAILEY
District 3

BRYAN DESLOGE
District 4

KRISTIN DOZIER
District 5

NICK MADDOX
At-Large

AKIN AKINYEMI
At-Large

PARWEZ ALAM
County Administrator

HERBERT W.A. THIELE
County Attorney

March 3, 2011

RE: RFP Title: Request for Proposals for Civil Engineering Services, Continuing Supply
Proposal Number: BC-03-17-11-25
Opening Date: Thursday, March 17, 2011 at 2:00 PM

ADDENDUM #1

Dear Vendor:

This letter serves as Addendum #1 for the above referenced project.

1. There have been many inquiries about the format and number of proposals needed as stated in Section II B. Here is a restatement of what is being requested:
 - a. There is to be one "Original" that contains the general section and a section of the specific information for each of the work categories you submit, an all inclusive "book".
 - b. For each work category to which you respond there are to be 3 copies that contain the general section and the specific information requested for the work category. These are to be the working sets for the Evaluation Committees.
2. In Section IV, Specific Proposal Information to be Provided for Each Work Category, the following items need correction:
 - B.1.d. "Project user agency's representative name, address and phone number." This is a duplicate of the previous item but with a different title for the representative and is to be ignored.
 - B.3. and B.4. are identical. Ignore B.4., the second one
3. The Insurance Certification Form was omitted from the RFP and is attached for completion and submittal.

Acknowledgment of this addendum is required as part of your submittal. Failure to acknowledge this addendum may result in rejection of your proposal.

Should you have any questions, feel free to call me at (850) 606-1600.

Sincerely,

Handwritten signature of Keith M. Roberts in black ink.

Keith M. Roberts
Purchasing Director

Deductibles and Self-Insured Retentions

Any deductibles or self-insured retentions must be declared to and approved by the County. At the option of the County, either: the insurer shall reduce or eliminate such deductibles or self-insured retentions as respects the County, its officers, officials, employees and volunteers; or the Contractor shall procure a bond guaranteeing payment of losses and related investigations, claim administration and defense expenses.

Endorsements to insurance policies will be provided as follows:

Additional insured (Leon County, Florida, its Officers, employees and volunteers) -
General Liability & Automobile Liability

Primary and not contributing coverage-
General Liability & Automobile Liability

Waiver of Subrogation (Leon County, Florida, its officers, employees and volunteers)- General
Liability, Automobile Liability, Workers' Compensation and Employer's Liability

Thirty days advance written notice of cancellation to County - General Liability,
Automobile Liability, Worker's Compensation & Employer's Liability.

Professional Liability Policy Declaration sheet as well as claims procedures for each applicable policy to be provided

Please mark the appropriate box:

Coverage is in place Coverage will be placed, without exception

The undersigned declares under penalty of perjury that all of the above insurer information is true and correct.

Name Alan Wise
Typed or Printed

Signature 

Date 3/16/11

Title Project Manager
(Company Risk Manager or Manager with Risk Authority)

CERTIFICATE OF LIABILITY INSURANCE

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).


PRODUCER ISU Suncoast Insurance Assoc P.O. Box 22668 Tampa, FL 33622-2668 813 289-5200	CONTACT NAME: PHONE (A/C, No, Ext): 813 289-5200		FAX (A/C, No): 8132894561
	E-MAIL ADDRESS: PRODUCER CUSTOMER ID #:		
INSURED Preble - Rish, Inc. 324 Marina Drive Port Saint Joe, FL 32547	INSURER(S) AFFORDING COVERAGE		NAIC #
	INSURER A : Phoenix Insurance Company		25623
	INSURER B : Travelers Indemnity Company		25658
	INSURER C : XL Specialty Insurance Company		37885
	INSURER D :		
	INSURER E :		

COVERAGES CERTIFICATE NUMBER: REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL INSR	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS	
A	GENERAL LIABILITY			6808149L113	02/16/2011	02/16/2012	EACH OCCURRENCE	\$2,000,000
	<input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY						DAMAGE TO RENTED PREMISES (Ea occurrence)	\$1,000,000
	<input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR						MED EXP (Any one person)	\$10,000
							PERSONAL & ADV INJURY	\$2,000,000
							GENERAL AGGREGATE	\$4,000,000
							PRODUCTS - COMP/OP AGG	\$4,000,000
								\$
								\$
								\$
								\$
B	<input checked="" type="checkbox"/> UMBRELLA LIAB			CUP8412Y959	02/16/2011	02/16/2012	EACH OCCURRENCE	\$1,000,000
	<input type="checkbox"/> EXCESS LIAB						AGGREGATE	\$1,000,000
	<input type="checkbox"/> DEDUCTIBLE							\$
	<input checked="" type="checkbox"/> RETENTION \$ 10000							\$
								\$
								\$
								\$
								\$
								\$
								\$
C	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY			DPR9690362	11/27/2010	11/27/2011	WC STATUTORY LIMITS	
	ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH)	Y/N	N/A				E.L. EACH ACCIDENT	\$
	If yes, describe under DESCRIPTION OF OPERATIONS below						E.L. DISEASE - EA EMPLOYEE	\$
							E.L. DISEASE - POLICY LIMIT	\$
	Professional Liability						\$1,000,000 per claim	
							\$1,000,000 annl aggr.	

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (Attach ACORD 101, Additional Remarks Schedule, if more space is required)
Professional liability is written on a claims made and reported basis.

CERTIFICATE HOLDER For Proposal Purposes	CANCELLATION SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS. AUTHORIZED REPRESENTATIVE 
--	--



PREBLE-RISH INC
CONSULTING ENGINEERS & SURVEYORS

STORMWATER ENGINEERING

A. ABILITY OF PROFESSIONAL PERSONNEL

Mr. Alan Wise is a Project Manager for PRI and will be responsible for overseeing each project with Leon County. **Employed with Preble-Rish, Inc. (PRI) since August 2010**, Mr. Wise has extensive experience in concept plans, site planning, cost estimating, design and permitting of commercial and residential projects all over Northwest Florida. He has a strong background in site development for private-sector clients with both commercial and residential developments. Mr. Wise has experience with AutoCad, ICPR3 with PercPack, Hydraflow, Flowmaster, and Ponds Software packages. Stormwater permitting experience through City of Tallahassee, Leon County, FDEP, Northwest Florida Water Management District, St. Johns River Water Management District, and Suwannee River Water Management District. Utility Permitting experience through FDEP, City of Tallahassee, City of Port St. Joe, Talquin Electric Cooperative, and others. Roadway /access design permitting experience through FDOT, Leon County, and the City of Tallahassee. Mr. Wise is currently involved with various projects in Wakulla, Leon, and Jefferson Counties.

Mr. Cliff Wilson is also a Project Manager for PRI and will be assisting Alan Wise with any stormwater engineering project for Leon County. **Employed with Preble-Rish, Inc. (PRI) since August 2005**, Mr. Wilson has worked on various types of civil design projects, permitting projects, and hydraulic water modeling.

B. EXPERIENCE WITH PROJECTS OF A SIMILAR TYPE AND SIZE

Below are a few of the projects that will show our experience in stormwater:

Buck Griffin Lake is a regional stormwater pond that treats approximately 3,000 acres of partially developed land. This project is located in Port St. Joe, Florida and was completed in 2007 for the City of Port St. Joe, 305 Cecil G. Costin Sr. Blvd., Port St. Joe, FL 32456. Contact information is Mr. Charlie Weston @ 850.229.8261. This project was funded by the Northwest Florida Water Management District (NFWMD) and was ranked number one in the state of Florida. PRI was responsible for the concept plan, grant preparation, and the design.



Baltzell Pond was also funded through the NFWFMD and this facility treats stormwater from the downtown area in Port St. Joe, Florida. This project was completed in 2007 for the City of Port St. Joe, 305 Cecil G. Costin Sr. Blvd., Port St. Joe, FL 32456. Contact information is Mr. Charlie Weston @ 850.229.8261. PRI was responsible for the concept plan, grant preparation, and the design.





Americus Ditch, also located in Port St. Joe, FL was a large open ditch which created maintenance and safety problems. This project was completed in 2008 for Gulf County, Florida, 1000 Cecil G. Costin Sr. Blvd, Port St. Joe, FL 32456. Contact information is Mr. Don Butler, County Administrator @ 850.229.6111. PRI designed and permitted a double swale closed ditch system (Americus Avenue Ditch) that is able to treat and collect all stormwater from the St. Joe Beach community before discharge into the Gulf of Mexico.



DUNE LAKE MANAGEMENT

Client: Walton County Board of County Commissioners
Reference: Ronnie Bell, (850) 892-8155
Description: Walton County uniquely has several dune lakes along the Gulf of Mexico. These lakes are fresh water fed and occasionally become tidal when they are open to the Gulf. When they are impounded by the natural dynamics of the beach, the rising water presents a hazard to the health and safety of the lakeside residents. Preble-Rish, Inc. is working with Walton County on a plan/permit for the management of the water levels in the dune lakes. Preble-Rish, Inc. prepares emergency permit requests to lower the water levels in the lakes when conditions justify it.

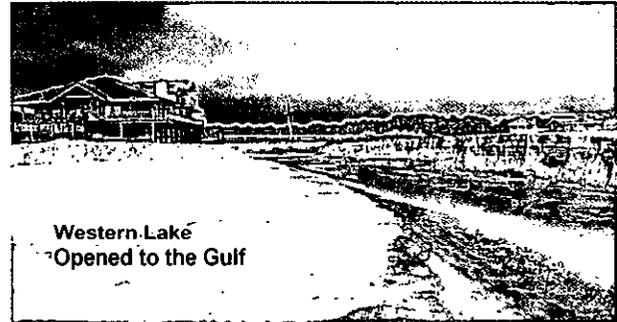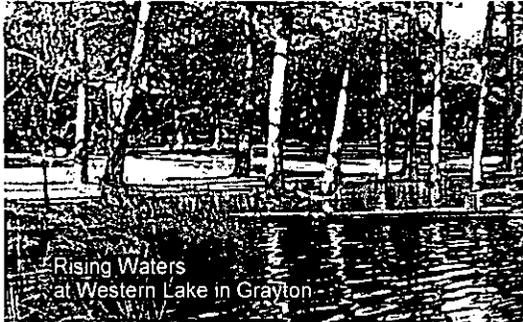

C. WILLINGNESS TO MEET SCHEDULE AND BUDGET REQUIREMENTS

Our team understands the importance of a complete and realistic project schedule. Upon receipt of a Notice to Proceed, our project team will take steps to ensure that project startup is a success and that it carries through to the end of the project schedule. Team members have an understanding of their roles and responsibilities as well as how their efforts are interrelated and have an effect on the rest of the project team. Open communication with the client and regulatory entities is paramount in maintaining a project schedule and budget.

D. EFFECT OF FIRM'S RECENT, CURRENT AND PROJECTED WORKLOAD

Over the past 5 years, PRI only lost 25% of its workforce due to the economy. Other firms reduced their size by 50% or more and some even closed their business. We feel that this demonstrates our strength in service to our current government clients. Our current workload is such that Preble-Rish, Inc. will be able to provide prompt and professional services to Leon County. PRI currently has the necessary staff to support the County's needs in a prompt and efficient manner.

E. EFFECT OF PROJECT TEAM LOCATION

Any stormwater project that PRI will perform for Leon County will be handled out of our Crawfordville office and managed by Mr. Alan Wise. However, our wide-area network allows us to efficiently utilize the services of our professional staff from any office, on any job, while managing the project from its nearest and most logical location.]

F. APPROACH TO THE PROJECT

Our approach is to keep you informed and up to date on project issues, communications and agency meetings. We will do so in a way that does not impose undue burden on the County. We will handle our responsibilities in an independent and professional manner while making sure that all decisions relating to the stormwater facilities are in keeping with the intentions of the scope of work as well as the desire of the County and its residents.



PREBLE-RISH INC
CONSULTING ENGINEERS & SURVEYORS

ROADWAY DESIGN

A. ABILITY OF PROFESSIONAL PERSONNEL

Mr. Alan Wise is a Project Manager for PRI and will be responsible for overseeing each project with Leon County. **Employed with Preble-Rish, Inc. (PRI) since August 2010**, Mr. Wise has extensive experience in concept plans, site planning, cost estimating, design and permitting of commercial and residential projects all over Northwest Florida. He has a strong background in site development for private-sector clients with both commercial and residential developments. Mr. Wise has experience with AutoCad, ICPR3 with PercPack, Hydraflow, Flowmaster, and Ponds Software packages. Stormwater permitting experience through City of Tallahassee, Leon County, FDEP, Northwest Florida Water Management District, St. Johns River Water Management District, and Suwannee River Water Management District. Utility Permitting experience through FDEP, City of Tallahassee, City of Port St. Joe, Talquin Electric Cooperative, and others. Roadway /access design permitting experience through FDOT, Leon County, and the City of Tallahassee. Mr. Wise is currently involved with various projects in Wakulla, Leon, and Jefferson Counties.

Mr. Travis Justice is a Senior Project Manager and Associate for PRI and will be assisting Mr. Alan Wise with each road project with Leon County. **Employed with Preble-Rish, Inc. (PRI) since January 2003**, Mr. Justice has worked on various types of civil design projects, which include the design of water and wastewater collection systems, stormwater design, roadway design, preliminary engineering reports, and construction cost estimates. Mr. Justice now serves as the Assistant Office Manager in our Panama City Office. He supervises approximately 23 office staff including engineers, cadd technicians and administrative staff. Mr. Justice has seven (7) years of experience in roadway and drainage design. He also has some program management and planning experience from previous employments.

B. EXPERIENCE WITH PROJECTS OF A SIMILAR TYPE AND SIZE





GADSDEN COUNTY - COUNTY ROAD 65 B

Client:	Gadsden County
Reference:	Mr. Robert Presnell (850) 875-8672
Location of Project:	Gadsden County
Project Cost:	\$2 Million
Project Schedule:	Project was completed in 2007
Brief Description:	This project consisted of resurfacing, reworking shoulders, replacing guardrail and installing reflective pavement markers.




GADSDEN COUNTY - HANNA MILL POND ROAD

Client: Gadsden County
Reference: Mr. Robert Presnell (850) 875-8672
Location of Project: Gadsden County
Project Cost: \$700,000
Project Schedule: Project was completed in 2008
Brief Description: This project consisted of widening and resurfacing, rip rap, ditch paving, reworking shoulders, striping, and installing reflective pavement markers.

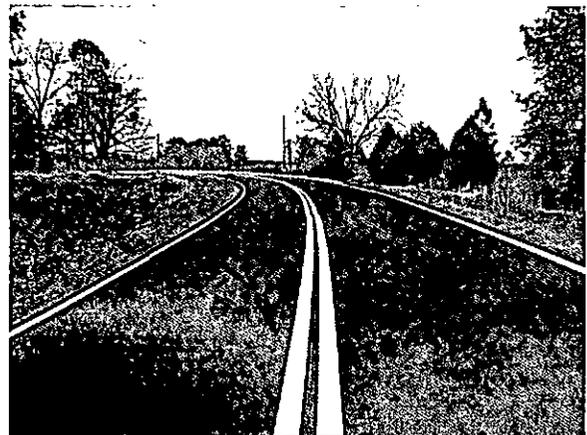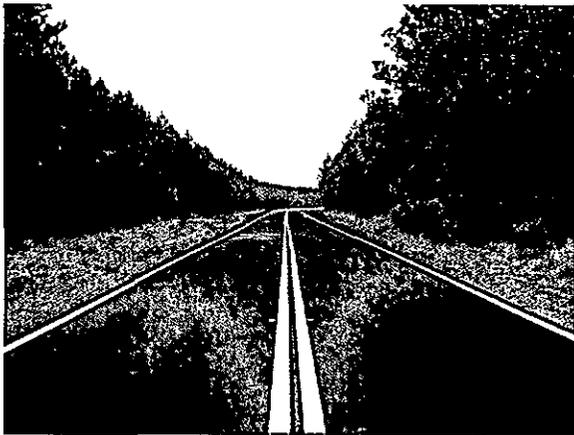

CALHOUN COUNTY - C.R. 275 RESURFACING AND WIDENING PROJECT

Client: Calhoun County
Reference: Mr. Sonny O'Bryan (850) 674-8075
Location of Project: Calhoun County
Project Cost: \$3.5 Million
Project Schedule: Project was completed in December 2006
Brief Description: This project consisted of 15 miles of widening, resurfacing, culvert extensions, ditch paving, shoulder reconstruction, and pavement markings.

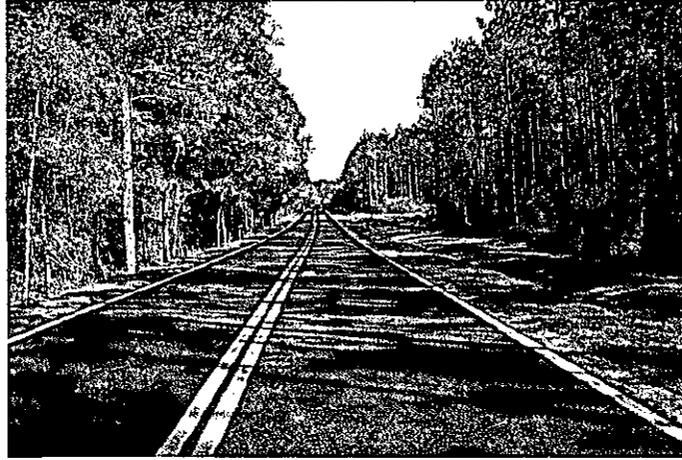

CALHOUN COUNTY - LAMB EDDY ROAD STORMWATER – FLORIDA FOREVER PROJECT

Client: Calhoun County
Reference: Sonny O'Bryan, (850) 674-8075
Location of Project: Calhoun County
Project Cost: \$450,000
Project Schedule: Project was completed in 2008
Brief Description: This project consisted of creating stormwater treatment swales and paving the roadway with pervious open grade hotmix.

C. WILLINGNESS TO MEET SCHEDULE AND BUDGET REQUIREMENTS

Our team understands the importance of a complete and realistic project schedule. Upon receipt of a Notice to Proceed, our project team will take steps to ensure that project startup is a success and that it carries through to the end of the project schedule. Team members have an understanding of their roles and responsibilities as well as how their efforts are interrelated and have an effect on the rest of the project team. Open communication with the client and regulatory entities is paramount in maintaining a project schedule and budget.

D. EFFECT OF FIRM'S RECENT, CURRENT AND PROJECTED WORKLOAD

Over the past 5 years, PRI only lost 25% of its workforce due to the economy. Other firms reduced their size by 50% or more and some even closed their business. We feel that this demonstrates our strength in service to our current government clients. Our current workload is such that Preble-Rish, Inc. will be able to provide prompt and professional services to Leon County. PRI currently has the necessary staff to support the County's needs in a prompt and efficient manner.

E. EFFECT OF PROJECT TEAM LOCATION

Any roadway design project that PRI will perform for Leon County will be handled out of our Crawfordville office and managed by Mr. Alan Wise. However, our wide-area network allows us to efficiently utilize the services of our professional staff from any office, on any job, while managing the project from its nearest and most logical location.

F. APPROACH TO THE PROJECT

Our approach is to keep you informed and up to date on project issues, communications and agency meetings. We will do so in a way that does not impose undue burden on the County. We will handle our responsibilities in an independent and professional manner while making sure that all decisions relating to roadway design are in keeping with the intentions of the scope of work as well as the desire of the County and its residents.



PREBLE-RISH INC
CONSULTING ENGINEERS & SURVEYORS


STRUCTURAL ENGINEERING

A. ABILITY OF PROFESSIONAL PERSONNEL

Mr. Alan Wise is a Project Manager for PRI and will be responsible for overseeing each project with Leon County. **Employed with Preble-Rish, Inc. (PRI) since August 2010**, Mr. Wise has extensive experience in concept plans, site planning, cost estimating, design and permitting of commercial and residential projects all over Northwest Florida. He has a strong background in site development for private-sector clients with both commercial and residential developments. Mr. Wise has experience with AutoCad, ICPR3 with PercPack, Hydraflow, Flowmaster, and Ponds Software packages. Stormwater permitting experience through City of Tallahassee, Leon County, FDEP, Northwest Florida Water Management District, St. Johns River Water Management District, and Suwannee River Water Management District. Utility Permitting experience through FDEP, City of Tallahassee, City of Port St. Joe, Talquin Electric Cooperative, and others. Roadway /access design permitting experience through FDOT, Leon County, and the City of Tallahassee. Mr. Wise is currently involved with various projects in Wakulla, Leon, and Jefferson Counties.

Mr. Clifford Knauer is a Firm Principal and Senior Project Manager with PRI. **Mr. Knauer has been employed with Preble-Rish, Inc. (PRI) since March of 1998**. He has been directly responsible for design and production of construction plans that include concrete and timber bridges, urban & rural roadway vertical and horizontal realignments, drainage basin analysis, underground utilities, site development, FEMA disaster reconstruction projects, NRCS drainage projects, parks and recreation facilities, and construction inspection for several counties. Many of these projects included permitting through the Department of Environmental Protection, Army Corps of Engineers, U.S. Fish and Wildlife Services, NWFWMMD, and various other State and Federal Agencies in order to provide clearance and mitigation for construction.


B. EXPERIENCE WITH PROJECTS OF A SIMILAR TYPE AND SIZE



FOURMILE CREEK PARK
Freeport, FL
CLIENT CONTACT:
Mayor Mickey Marse
P.O. Box 339
Freeport, FL
850.835.2822


This project consisted of the design, inspection, and construction of an asphalt parking area with boat ramp and loading dock. Public restrooms, stormwater facilities, a 640 linear foot timber boardwalk, and a gazebo were constructed on-site in addition to a 365 linear foot steel sheet pile retaining wall.

Construction Cost: \$1,300,000.00



EMERGENCY OPERATIONS CENTER Washington Co., FL
CLIENT CONTACT:
County Administrator
Washington Co. BOCC
850.638.6200

This project consists of the design, permitting, survey, construction administration and inspection of a 3000 S.F. concrete structure and site improvements. The structure is concrete cinder block exterior walls and is engineered to withstand a cat 5 hurricane (155 mph winds). Construction Cost: \$1,000,000.00

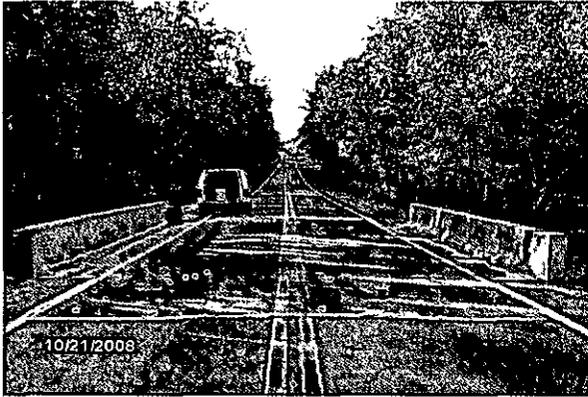

GADSDEN COUNTY – BEAR CREEK BRIDGE REPLACEMENT

*CLIENT CONTACT: Gadsden County
Gadsden Co. BOCC
850.875.8672*

This project consisted of replacing two structural plate arch pipes with a concrete bridge deck.

C. WILLINGNESS TO MEET SCHEDULE AND BUDGET REQUIREMENTS

Our team understands the importance of a complete and realistic project schedule. Upon receipt of a Notice to Proceed, our project team will take steps to ensure that project startup is a success and that it carries through to the end of the project schedule. Team members have an understanding of their roles and responsibilities as well as how their efforts are interrelated and have an effect on the rest of the project team. Open communication with the client and regulatory entities is paramount in maintaining a project schedule and budget.

D. EFFECT OF FIRM'S RECENT, CURRENT AND PROJECTED WORKLOAD

Over the past 5 years, PRI only lost 25% of its workforce due to the economy. Other firms reduced their size by 50% or more and some even closed their business. We feel that this demonstrates our strength in service to our current government clients. Our current workload is such that Preble-Rish, Inc. will be able to provide prompt and professional services to Leon County. PRI currently has the necessary staff to support the County's needs in a prompt and efficient manner.

E. EFFECT OF PROJECT TEAM LOCATION

Any structural engineering project that PRI will perform for Leon County will be handled out of our Crawfordville office and managed by Mr. Alan Wise. However, our wide-area network allows us to efficiently utilize the services of our professional staff from any office, on any job, while managing the project from its nearest and most logical location.

F. APPROACH TO THE PROJECT

Our approach is to keep you informed and up to date on project issues, communications and agency meetings. We will do so in a way that does not impose undue burden on the County. We will handle our responsibilities in an independent and professional manner while making sure that all decisions relating to the structural engineering projects are in keeping with the intentions of the scope of work as well as the desire of the County and its residents.



PREBLE-RISH INC
CONSULTING ENGINEERS & SURVEYORS

CONSTRUCTION ENGINEERING AND INSPECTION SERVICES

A. ABILITY OF PROFESSIONAL PERSONNEL

Preble-Rish, Inc. offers construction administration and inspection to compliment a wide range of projects. Our experienced staff can keep any job running smoothly. We feel that on-site inspection is a vital part of all projects. PRI currently has **12 qualified Inspectors** on staff to provide our clients with inspection services. PRI also reviews pay requests, attends progress meetings with the client and the contractor, as well as certifies the project once construction is complete.

Eric Pitts is our Inspection Manager and is also an Associate with PRI. **Employed with Preble-Rish, Inc. (PRI) since August 2000**, Mr. Pitts is responsible for the direct supervision of twelve inspectors over a sixteen-county area. Once contracts are awarded to PRI, Mr. Pitts has the responsibility of reviewing the projects and assigning them to the inspector that he feels is most qualified to oversee that particular project. Mr. Pitts and the other inspectors then conduct inspections on the many various types of civil, environmental, and construction design projects. These projects include water distribution/pumping facilities, wastewater collection systems, treatment plants, large transmission mains, stormwater systems, structural projects, extensive dredge and fill projects, boat ramps, bridge projects, pipe placement, road resurfacing, new road construction, and subdivisions. Mr. Pitts is responsible for the design and permitting of various utility projects. Mr. Pitts also has the responsibility of QA/QC of all PRI inspectors.

B. EXPERIENCE WITH PROJECTS OF A SIMILAR TYPE AND SIZE

Location	Project Name	Funding	Year	Inspector
City of Port St. Joe	Sunset Circle Drainage Improvements	USDA	2009	Jeff Hinote
City of Port St. Joe	White City Sewer Transmission/Collection	FDEP	2008	Jeff Hinote
City of Port St. Joe	Basin 7 Rehab	Bond	2009	Jeff Hinote
City of Port St. Joe	Culvert Replacement, 8 th Street	FEMA	2006	Jeff Hinote
City of Port St. Joe	Frank Pate Park Improvements	FRDAP	2009	Jeff Hinote
City of Port St. Joe	Overstreet Water Extension Ph 1B	Bond	2009	Jeff Hinote
City of Port St. Joe	PSJ Commerce Park Ph. II	Private	2007	Jeff Hinote
City of Port St. Joe	Cape San Blas Sewer Extension	Dev.	2005	Jeff Hinote
City of Port St. Joe	City Hall Parking Lot	Bond	2009	Darren Evers
City of Port St. Joe	Williams Avenue Improvements	USDA	2009	Darren Evers
City of Port St. Joe	Windmark Master Lift Station	Bond	2008	Darren Evers
City of Port St. Joe	St. Joe Beach Sewer	Bond	2009	Darren Evers
City of Port St. Joe	Overstreet Phase II Water	Bond	2009	Darren Evers
City of Port St. Joe	St. Joe Beach Booster Plant	Bond	2009	Darren Evers
City of Port St. Joe	Windmark Offsite Utilities	Bond	2008	Darren Evers
City of Wewa	Lake Grove Waterline Extension	Budget	2008	Jeff Hinote
City of Wewa	Water and Wastewater System Impr.	Grant	2008	Jeff Hinote
Franklin County	Twin Lakes Road Paving, Stormwater Impr	Grant	2008	Jeff Hinote
Gulf County	Americus Avenue Resurfacing	Bond	2008	Jeff Hinote
Gulf County	Sunset Village Subdivision	Private	2006	Jeff Hinote
Gulf County	Road Bond	Bond	2009	Jeff Hinote
Gulf County	Cape San Blas Multi-Use Path	FDOT	2008	Darren Evers

County	Location/Subdivision	Private	2008	Darren Evers
Calhoun County	CR 275 Widening and Resurfacing	SCOP	2006	Berry Fant/ Matt Carpenter
Calhoun County	Abe Springs/Bullhead Bay Road Paving	CIGP	2006	Berry Fant/ Matt Carpenter
Calhoun County	Mason Road Paving	CIGP	2006	Buddy Kennington/ Matt Carpenter
Calhoun County	CR 275 North Widening and Resurfacing	SCOP	2007	Berry Fant/ Matt Carpenter
Calhoun County	Magnolia Church Road Widening and Resurfacing	SCRAP	2007	Buddy Kennington/ Matt Carpenter
Calhoun County	John Redd Road East Paving	CIGP	2007	Buddy Kennington/ Matt Carpenter
Gadsden County	CR 65 Resurfacing	SCRAP	2006	Berry Fant/ Matt Carpenter
Gadsden County	CR 12 Resurfacing	SCOP	2006	Berry Fant/ Matt Carpenter
Gadsden County	Iron Bridge Road Resurfacing	CIGP	2006	Berry Fant/ Matt Carpenter
Gadsden County	CR 65B Resurfacing	SCRAP	2007	Berry Fant/ Matt Carpenter
Gadsden County	Juniper Road Resurfacing	SCRAP	2007	Berry Fant/ Matt Carpenter
Gadsden County	Lanier Road Resurfacing	SCOP	2007	Berry Fant/ Matt Carpenter
Gadsden County	Atwater Road Resurfacing	CIGP	2007	Berry Fant/ Matt Carpenter
Liberty County	CR 270/271 Resurfacing	CIGP	2006	Matt Carpenter
Liberty County	CR 12 Widening and Resurfacing	SCOP	2006	Berry Fant/ Matt Carpenter
Liberty County	Torrea Park Road Resurfacing	CIGP	2007	Buddy Kennington/ Matt Carpenter
Wakulla County	C.R. 367 Resurfacing	SCRAP	2009	Blake Rish
Wakulla County	C.R. 367A Widening & Resurfacing	SCOP	2009	Blake Rish

C. WILLINGNESS TO MEET SCHEDULE AND BUDGET REQUIREMENTS

Our team understands the importance of a complete and realistic project schedule. Upon receipt of a Notice to Proceed, our project team will take steps to ensure that project startup is a success and that it carries through to the end of the project schedule. Team members have an understanding of their roles and responsibilities as well as how their efforts are interrelated and have an effect on the rest of the project team. Open communication with the client and regulatory entities is paramount in maintaining a project schedule and budget.

D. EFFECT OF FIRM'S RECENT, CURRENT AND PROJECTED WORKLOAD

Over the past 5 years, PRI only lost 25% of its workforce due to the economy. Other firms reduced their size by 50% or more and some even closed their business. We feel that this demonstrates our strength in service to our current government clients. Our current workload is such that Preble-Rish, Inc. will be able to provide prompt and professional services to Leon County. PRI currently has the necessary staff to support the County's needs in a prompt and efficient manner.

E. EFFECT OF PROJECT TEAM LOCATION

Any construction engineering and inspection project that PRI will perform for Leon County will be handled out of our Crawfordville office and managed by Mr. Alan Wise and assisted by Mr. Eric Pitts. However, our wide-area network allows us to efficiently utilize the services of our professional staff from any office, on any job, while managing the project from its nearest and most logical location.

F. APPROACH TO THE PROJECT

Our approach is to keep you informed and up to date on project issues, communications and agency meetings. We will do so in a way that does not impose undue burden on the County. We will handle our responsibilities in an independent and professional manner while making sure that all decisions relating to the construction engineering and inspection are in keeping with the intentions of the scope of work as well as the desire of the County and its residents.



PREBLE-RISH INC
CONSULTING ENGINEERS & SURVEYORS

SURVEYING

A. ABILITY OF PROFESSIONAL PERSONNEL

Mr. Alan Wise is a Project Manager for PRI and will be responsible for overseeing each project with Leon County. **Employed with Preble-Rish, Inc. (PRI) since August 2010**, Mr. Wise has extensive experience in concept plans, site planning, cost estimating, design and permitting of commercial and residential projects all over Northwest Florida. He has a strong background in site development for private-sector clients with both commercial and residential developments. Mr. Wise has experience with AutoCad, ICPR3 with PercPack, Hydraflow, Flowmaster, and Ponds Software packages. Stormwater permitting experience through City of Tallahassee, Leon County, FDEP, Northwest Florida Water Management District, St. Johns River Water Management District, and Suwannee River Water Management District. Utility Permitting experience through FDEP, City of Tallahassee, City of Port St. Joe, Talquin Electric Cooperative, and others. Roadway /access design permitting experience through FDOT, Leon County, and the City of Tallahassee. Mr. Wise is currently involved with various projects in Wakulla, Leon, and Jefferson Counties.

Mr. David Bartlett is the Survey Manager and also an Associate with PRI. **As a Professional Land Surveyor (PLS) with Preble-Rish, Inc. (PRI) since May 2002** (over 39 years' total experience), Mr. Bartlett's responsibilities include the supervision of 4 field crews. Additional duties are to quality assure Cad pool's production of mapping and verify that the survey meets the standards set forth by governing bodies (Local, State and National) prior to review and release to the client/public. Mr. Bartlett also completes records research, calculations, legal description writing and quality control to assure the final product meets the client/requirement. Representative experience includes: design, right-of-way and construction surveying, boundary, right-of-way, as-built, construction layout, topographic, hydrographic, quantity, record, mean high water line and special purpose surveys. Mr. Bartlett has previous work experience in Leon County from 1972 through 1999. A few of the survey projects he was involved in was Tallahassee Memorial Hospital, Tallahassee Community Hospital, Campbell Stadium, Rickards, Leon, and Lincoln High Schools, Carolyn Brevard Elementary school, Tallahassee Mall and also Governor Square Mall.

B. EXPERIENCE WITH PROJECTS OF A SIMILAR TYPE AND SIZE

WHITE CITY SEWER

Client: City of Port St. Joe
Reference: Charlie Weston, -- [850] 229-8261
Location of Project: White City, FL
Project Cost: \$4.2 Million
Project Schedule: Construction to begin in 2009

Brief Description of Project: This project will provide sewer service to the White City area. This project consists of pressure sewer collection system, one lift station and an 8 inch forcemain capable of transmitting sewage from 500 customers currently served by individual septic systems. The pressure sewer collection system consists of 29,000 LF of 2", 3", 4", and 6" force main and 150 individual grinder stations. The lift station is composed of one 8 ft diameter wet well with two 425 gpm pumps. The 8" PVC forcemain extends five miles from White City to Port St. Joe.

OVERSTREET WATER SYSTEM

Client: City of Port St. Joe
Reference: Charlie Weston, - [850] 229-8261
Location of Project: Overstreet, FL
Project Cost: \$4.2 Million
Project Schedule: Project is under construction.

Brief Description of Project: This project consists of upgrades to existing St. Joe Beach Booster Plant and water transmission main extension to serve the Overstreet area. The water booster plant upgrades include five booster pumps capable of delivering 2,260 gpm. Variable frequency drives are used to control the pumps and maintain water pressure in the system. All of the equipment is installed in a climate controlled building. The transmission main from St. Joe Beach to Overstreet consists of 45,000 LF of 10" and 12" PVC pipe and fire hydrants every 2,000 ft.

CALHOUN COUNTY - C.R. 286

Client: Calhoun County
Reference: Mr. Sonny O'Bryan (850) 674-8075
Location of Project: Calhoun County
Project Cost: \$1.3 Million
Project Schedule: Project was completed in 2008

Brief Description: This project consisted of widening, constructing paved shoulders, resurfacing, replacing guardrail, reworking shoulders, striping, and installing reflective pavement markers.

CALHOUN COUNTY - LAMB EDDY ROAD STORMWATER – FLORIDA FOREVER PROJECT

Client: Calhoun County
Reference: Sonny O'Bryan, (850) 674-8075
Location of Project: Calhoun County
Project Cost: \$450,000
Project Schedule: Project was completed in 2008

Brief Description: This project consisted of creating stormwater treatment swales and paving the roadway with pervious open grade hotmix.

SOUTHPORT - MASTER LIFT STATION & FORCE MAINS

Client: GCEC/Bay County
Reference: Mr. Michael White, GCEC (850) 814-3770
Location of Project: Southport, Florida
Completion Date: 2007/2009 (2 years / 3 phases)

Brief Description: The project consisted of 6" through 18" pipe, PVC and HDPE were used as the master portion of the system to serve the SR 77 Corridor and unincorporated Southport area over to Deerpoint Lake. Phase I was previously installed to serve the Fanning Bayou Development on CR 2300. Phase II will be installed in the next six (6) months and Phase III is on hold until developments along Edwards Road and Resota Beach Road are further along in the development stage. PRI has been responsible for all surveying and engineering components of this project.

MCELVEY WATER STORAGE AND PUMP STATION IMPROVEMENTS

Client: Panama City Beach, Florida
Reference: Mr. Al Shortt, PE/Utility Services Director (850) 258-4231
Location of Project: Panama City Beach, Florida
Completion Date: 2008

Brief Description: Firm's responsibility included design, permitting, and construction administration for a plant upgrade to include new high service pumps, sodium hydrochlorite system and surge system.

C. WILLINGNESS TO MEET SCHEDULE AND BUDGET REQUIREMENTS

Our team understands the importance of a complete and realistic project schedule. Upon receipt of a Notice to Proceed, our project team will take steps to ensure that project startup is a success and that it carries through to the end of the project schedule. Team members have an understanding of their roles and responsibilities as well as how their efforts are interrelated and have an effect on the rest of the project team. Open communication with the client and regulatory entities is paramount in maintaining a project schedule and budget.

D. EFFECT OF FIRM'S RECENT, CURRENT AND PROJECTED WORKLOAD

Over the past 5 years, PRI only lost 25% of its workforce due to the economy. Other firms reduced their size by 50% or more and some even closed their business. We feel that this demonstrates our strength in service to our current government clients. Our current workload is such that Preble-Rish, Inc. will be able to provide prompt and professional services to Leon County. PRI currently has the necessary staff to support the County's needs in a prompt and efficient manner.

E. EFFECT OF PROJECT TEAM LOCATION

Any surveying project that PRI will perform for Leon County will be handled out of our Crawfordville office and managed by Mr. Alan Wise. However, our wide-area network allows us to efficiently utilize the services of our professional staff from any office, on any job, while managing the project from its nearest and most logical location.

F. APPROACH TO THE PROJECT

Our approach is to keep you informed and up to date on project issues, communications and agency meetings. We will do so in a way that does not impose undue burden on the County. We will handle our responsibilities in an independent and professional manner while making sure that all decisions relating to the surveying projects are in keeping with the intentions of the scope of work as well as the desire of the County and its residents.



PREBLE-RISH INC
CONSULTING ENGINEERS & SURVEYORS

SUBDIVISION AND SITE DEVELOPMENT ENGINEERING


A. ABILITY OF PROFESSIONAL PERSONNEL

Mr. Alan Wise is a Project Manager for PRI and will be responsible for overseeing each project with Leon County. **Employed with Preble-Rish, Inc. (PRI) since August 2010**, Mr. Wise has extensive experience in concept plans, site planning, cost estimating, design and permitting of commercial and residential projects all over Northwest Florida. He has a strong background in site development for private-sector clients with both commercial and residential developments. Mr. Wise has experience with AutoCad, ICPR3 with PercPack, Hydraflow, Flowmaster, and Ponds Software packages. Stormwater permitting experience through City of Tallahassee, Leon County, FDEP, Northwest Florida Water Management District, St. Johns River Water Management District, and Suwannee River Water Management District. Utility Permitting experience through FDEP, City of Tallahassee, City of Port St. Joe, Talquin Electric Cooperative, and others. Roadway /access design permitting experience through FDOT, Leon County, and the City of Tallahassee. Mr. Wise is currently involved with various projects in Wakulla, Leon, and Jefferson Counties.


Mr. Chris Forehand is a Firm Principal and Senior Project Manager for PRI. **Employed with Preble-Rish, Inc. (PRI) since May 1997**, Mr. Forehand has been responsible for various types of civil and environmental design projects, which include water distribution/pumping facilities, wastewater collection systems, effluent spray fields, large water transmission mains, stormwater systems, small structural projects, extensive dredge and fill permitting and all project associated permitting. Other responsibilities have included Federal and State funding applications for City/County governments on many different project types throughout the panhandle which include FRDAP, USDA Rural Development, SRF and CDBG funding programs. Mr. Forehand has been involved with numerous subdivisions in Walton, Bay, and Gulf Counties which range from 4 units to 2,000 units. In addition, Mr. Forehand has worked on many condominium developments as well as commercial site developments. Mr. Forehand serves many roles with the firm and provides quality control to the firm.

B. EXPERIENCE WITH PROJECTS OF A SIMILAR TYPE AND SIZE

PRI is FDOT certified in Land Planning and Engineering. PRI's staff has worked on many site planning and design projects which includes schools, colleges, prisons, City administration buildings, fire stations, court houses, high-rise condominiums, and other commercial site developments.

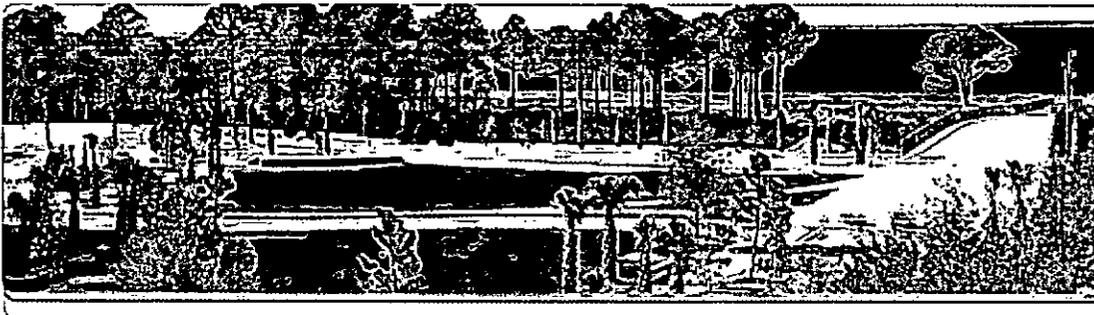

Windmark Beach, near Port St. Joe, Florida, is the panhandle's most ambitious project to date. The St. Joe Company is the developer of this 2,000 acre, 1662 unit community which includes highway relocation, and a future 18-hole golf course, along with other attractive amenities.

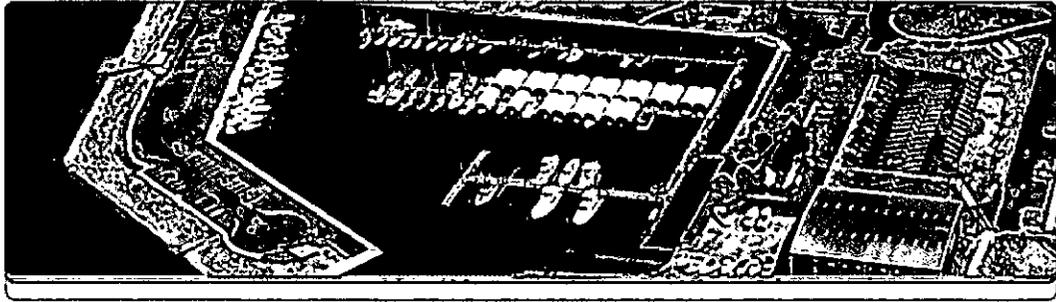

Port St. Joe Marina: This project was constructed for the City of Port St. Joe and consisted of the design and construction of a Gulf of Mexico accessed municipal marina for 120 wet slips, 100 dry slips and dry storage. The facility provides a fueling facility, restaurant, restrooms, and ship's store.

PROJECT NAME - Ovation

CLIENT – Ashwood Development

DESCRIPTION – New 120 lot subdivision at Cape San Blas. The project featured surveying, roadway, water, sewer and stormwater design, pool house with other amenities.

PROJECT NAME - Garrison Plantation

CLIENT – Jay Rish

DESCRIPTION - New 52-Lot Subdivision in Port St. Joe. The project featured roadway, water, sewer and stormwater design.

PROJECT NAME - Grammercy Plantation

CLIENT – Grammercy Plantation, L.L.C.

DESCRIPTION - This project consisted of a 400-acre development in Franklin County along U.S. Highway 98 including 162 residential lots, a 16-acre commercial area, and an 80-unit hotel as part of a local development order.

PROJECT NAME - Bayview Subdivision

CLIENT – St. Joe Land Company

DESCRIPTION - Extended residential area in Port St. Joe along St. Joe Bay. This project consisted of surveying, water and sewer design.

PROJECT NAME - Water's Edge Subdivision

CLIENT – Dale Piergiovanni

DESCRIPTION - New subdivision off of C-30A in Gulf County featured forty-five lots, including two gulf front lots. Project featured roadway, potable water, community septic, stormwater, tennis court, and club house.

C. WILLINGNESS TO MEET SCHEDULE AND BUDGET REQUIREMENTS

Our team understands the importance of a complete and realistic project schedule. Upon receipt of a Notice to Proceed, our project team will take steps to ensure that project startup is a success and that it carries through to the end of the project schedule. Team members have an understanding of their roles and responsibilities as well as how their efforts are interrelated and have an effect on the rest of the project team. Open communication with the client and regulatory entities is paramount in maintaining a project schedule and budget.

D. EFFECT OF FIRM'S RECENT, CURRENT AND PROJECTED WORKLOAD

Over the past 5 years, PRI only lost 25% of its workforce due to the economy. Other firms reduced their size by 50% or more and some even closed their business. We feel that this demonstrates our strength in service to our current government clients. Our current workload is such that Preble-Rish, Inc. will be able to provide prompt and professional services to Leon County. PRI currently has the necessary staff to support the County's needs in a prompt and efficient manner.

E. EFFECT OF PROJECT TEAM LOCATION

Any subdivision and site development engineering project that PRI will perform for Leon County will be handled out of our Crawfordville office and managed by Mr. Alan Wise. However, our wide-area network allows us to efficiently utilize the services of our professional staff from any office, on any job, while managing the project from its nearest and most logical location.

F. APPROACH TO THE PROJECT

Our approach is to keep you informed and up to date on project issues, communications and agency meetings. We will do so in a way that does not impose undue burden on the County. We will handle our responsibilities in an independent and professional manner while making sure that all decisions relating to the subdivision and site development engineering projects are in keeping with the intentions of the scope of work as well as the desire of the County and its residents.



PREBLE-RISH INC
CONSULTING ENGINEERS & SURVEYORS

PARKS AND RECREATION FACILITY ENGINEERING

A. ABILITY OF PROFESSIONAL PERSONNEL

Mr. Alan Wise is a Project Manager for PRI and will be responsible for overseeing each project with Leon County. **Employed with Preble-Rish, Inc. (PRI) since August 2010**, Mr. Wise has extensive experience in concept plans, site planning, cost estimating, design and permitting of commercial and residential projects all over Northwest Florida. He has a strong background in site development for private-sector clients with both commercial and residential developments. Mr. Wise has experience with AutoCad, ICPR3 with PercPack, Hydraflow, Flowmaster, and Ponds Software packages. Stormwater permitting experience through City of Tallahassee, Leon County, FDEP, Northwest Florida Water Management District, St. Johns River Water Management District, and Suwannee River Water Management District. Utility Permitting experience through FDEP, City of Tallahassee, City of Port St. Joe, Talquin Electric Cooperative, and others. Roadway /access design permitting experience through FDOT, Leon County, and the City of Tallahassee. Mr. Wise is currently involved with various projects in Wakulla, Leon, and Jefferson Counties.

Mr. Clifford Knauer is a Firm Principal and Senior Project Manager with PRI. **Mr. Knauer has been employed with Preble-Rish, Inc. (PRI) since March of 1998**. He has been directly responsible for design and production of construction plans that include concrete and timber bridges, urban & rural roadway vertical and horizontal realignments, drainage basin analysis, underground utilities, site development, FEMA disaster reconstruction projects, NRCS drainage projects, parks and recreation facilities, and construction inspection for several counties. Many of these projects included permitting through the Department of Environmental Protection, Army Corps of Engineers, U.S. Fish and Wildlife Services, NFWFMD, and various other State and Federal Agencies in order to provide clearance and mitigation for construction.

B. EXPERIENCE WITH PROJECTS OF A SIMILAR TYPE AND SIZE



CAMPBELL PARK





Campbell Park (Vernon, Florida) was completed in 2006 with assistance from the Florida Recreational Developmental Assistant Program. This project consisted of site and building design for public restrooms, parking area, basketball courts, children's playground, along with stormwater design and permitting.



COOPER RECREATIONAL PARK

This project, located in Calhoun County, consisted of renovations of the existing bathroom facilities, picnic pavilion, and the construction of new playground equipment, an asphalt walking trail, and the installation of ball field lighting.

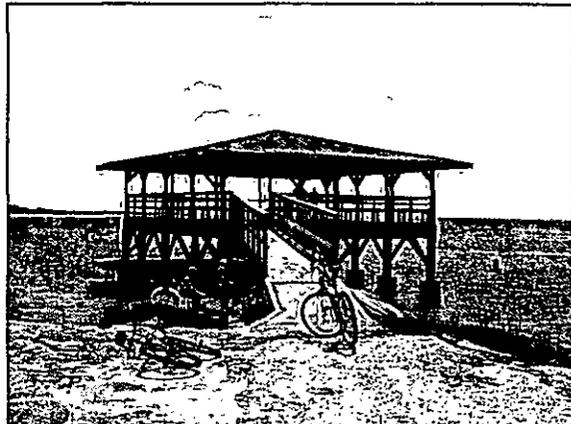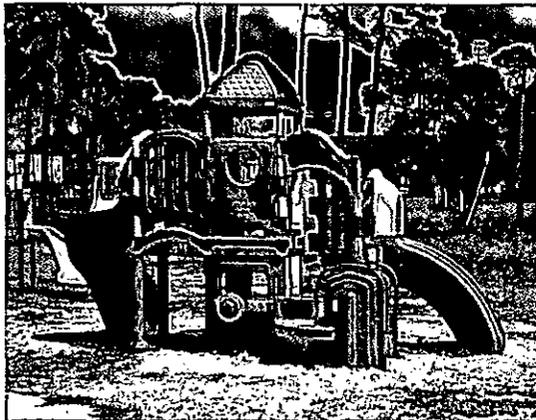


FRANK PATE PARK


This project is located in Port St. Joe next to St. Joseph Bay and contains a boat ramp, park docks, and a covered pavilion on St. Joe Bay.



LAMAR FAISON FIELDS

This project is located in Port St. Joe and consisted of two soccer fields, picnic gazebos with table, tot lot, playground for school age kids, and a nature walk.

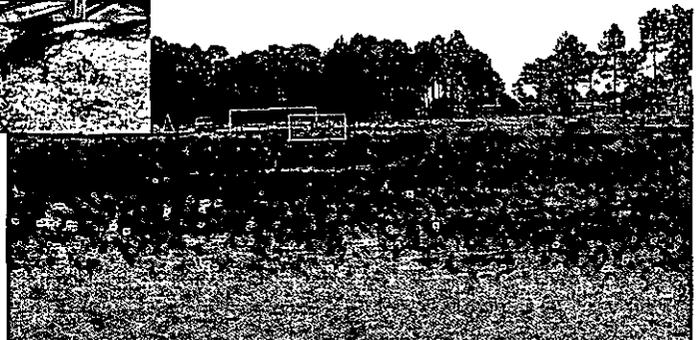

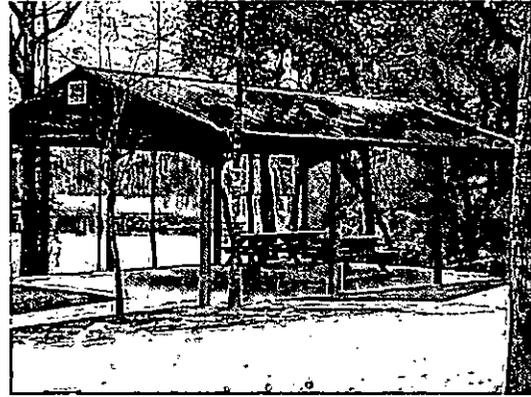



LITARD LOG PARK

Litard Log Park in Washington County included the design and construction of a boat ramp, dock, pavilion, restroom, entrance road, stormwater facility, and parking with handicap accessibility. Funding was provided by Florida Boating Improvement. Permitting agencies included Washington County Planning and Zoning and Florida Department of Environmental Protection.



WEE CARE PARK

Wee Care Park in Walton County included the design of a large County park for the surrounding community. Amenities included baseball fields, basketball courts, children's splash pad, and several other outdoor activities. Project consisted of master planning, site design, stormwater design and permitting, and quality control. Phase II was completed in June 2005.

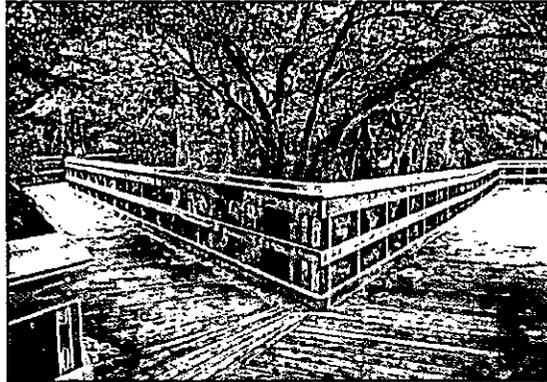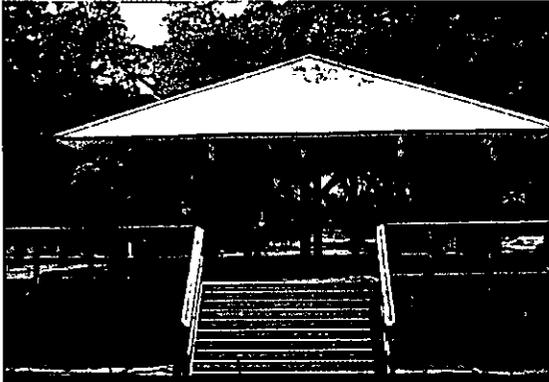

MORRISON SPRINGS IMPROVEMENTS

Morrison Springs Recreational Area is located in Walton County, Florida. This project consists of a parking area reconfiguration and several additional structures. This construction includes a timber boardwalk from the parking area to the water's edge, where an observation deck is located. In order to traverse wetlands along the roadway to the existing boat ramp and limit the impact on the wetlands, two timber bridges are in place. Other amenities include a new educational and recreational pavilion, improvements to the existing boat ramps, stormwater facilities, restroom facilities with showers, and a children's playground.

C. WILLINGNESS TO MEET SCHEDULE AND BUDGET REQUIREMENTS

Our team understands the importance of a complete and realistic project schedule. Upon receipt of a Notice to Proceed, our project team will take steps to ensure that project startup is a success and that it carries through to the end of the project schedule. Team members have an understanding of their roles and responsibilities as well as how their efforts are interrelated and have an effect on the rest of the project team. Open communication with the client and regulatory entities is paramount in maintaining a project schedule and budget.

D. EFFECT OF FIRM'S RECENT, CURRENT AND PROJECTED WORKLOAD

Over the past 5 years, PRI only lost 25% of its workforce due to the economy. Other firms reduced their size by 50% or more and some even closed their business. We feel that this demonstrates our strength in service to our current government clients. Our current workload is such that Preble-Rish, Inc. will be able to provide prompt and professional services to Leon County. PRI currently has the necessary staff to support the County's needs in a prompt and efficient manner.

E. EFFECT OF PROJECT TEAM LOCATION

Any parks and recreation facility project that PRI will perform for Leon County will be handled out of our Crawfordville office and managed by Mr. Alan Wise. However, our wide-area network allows us to efficiently utilize the services of our professional staff from any office, on any job, while managing the project from its nearest and most logical location.]

F. APPROACH TO THE PROJECT

Our approach is to keep you informed and up to date on project issues, communications and agency meetings. We will do so in a way that does not impose undue burden on the County. We will handle our responsibilities in an independent and professional manner while making sure that all decisions relating to the parks and recreation facilities are in keeping with the intentions of the scope of work as well as the desire of the County and its residents.



PREBLE-RISH INC
CONSULTING ENGINEERS & SURVEYORS

UTILITY ENGINEERING

A. ABILITY OF PROFESSIONAL PERSONNEL

Mr. Alan Wise is a Project Manager for PRI and will be responsible for overseeing each project with Leon County. **Employed with Preble-Rish, Inc. (PRI) since August 2010**, Mr. Wise has extensive experience in concept plans, site planning, cost estimating, design and permitting of commercial and residential projects all over Northwest Florida. He has a strong background in site development for private-sector clients with both commercial and residential developments. Mr. Wise has experience with AutoCad, ICPR3 with PercPack, Hydraflow, Flowmaster, and Ponds Software packages. Stormwater permitting experience through City of Tallahassee, Leon County, FDEP, Northwest Florida Water Management District, St. Johns River Water Management District, and Suwannee River Water Management District. Utility Permitting experience through FDEP, City of Tallahassee, City of Port St. Joe, Talquin Electric Cooperative, and others. Roadway /access design permitting experience through FDOT, Leon County, and the City of Tallahassee. Mr. Wise is currently involved with various projects in Wakulla, Leon, and Jefferson Counties.

Mr. Chris Forehand is a Firm Principal and Senior Project Manager for PRI. **Employed with Preble-Rish, Inc. (PRI) since May 1997**, Mr. Forehand has been responsible for various types of civil and environmental design projects, which include water distribution/pumping facilities, wastewater collection systems, effluent spray fields, large water transmission mains, stormwater systems, small structural projects, extensive dredge and fill permitting and all project associated permitting. Other responsibilities have included Federal and State funding applications for City/County governments on many different project types throughout the panhandle which include FRDAP, USDA Rural Development, SRF and CDBG funding programs. Mr. Forehand has been involved with numerous subdivisions in Walton, Bay, and Gulf Counties which range from 4 units to 2,000 units. In addition, Mr. Forehand has worked on many condominium developments as well as commercial site developments. Mr. Forehand serves many roles with the firm and provides quality control to the firm.


B. EXPERIENCE WITH PROJECTS OF A SIMILAR TYPE AND SIZE

LYNN HAVEN WATER PLANT IMPROVEMENTS & WELL NO. 6

Client: Panama City, Florida
Reference: Mr. Jim Slonina, PE (850) 763-5200
Location of Project: Lynn Haven, FL
Completion Date: 2008

Brief Description: Firm's responsibility included design, permitting and construction administration for a 2.0 MG ground storage tank and a 1,000 gpm 16" casing production well.



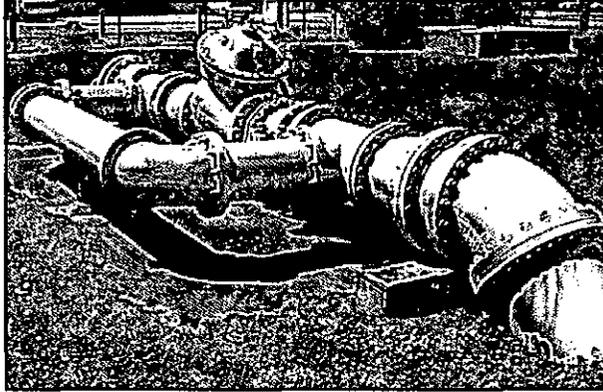

MCELVEY WATER STORAGE AND PUMP STATION IMPROVEMENTS

Client: Panama City Beach, Florida
Reference: Mr. Al Shortt, PE/Utility Services Director (850) 258-4231
Location of Project: Panama City Beach, Florida
Completion Date: 2008


Brief Description: Firm's responsibility included design, permitting, and construction administration for a plant upgrade to include new high service pumps, sodium hydrochlorite system and surge system.



PORT ST. JOE SURFACE WATER PLANT

Client: City of Port St Joe
Reference: Mr. John Grantland (850) 229-2221
Location of Project: Port St. Joe, Florida
Completion Date: 2008

Brief Description: Firm's responsibility included design, permitting, and construction administration for a 6.0 MGD surface water plant which treats water from the freshwater canal in Gulf County.

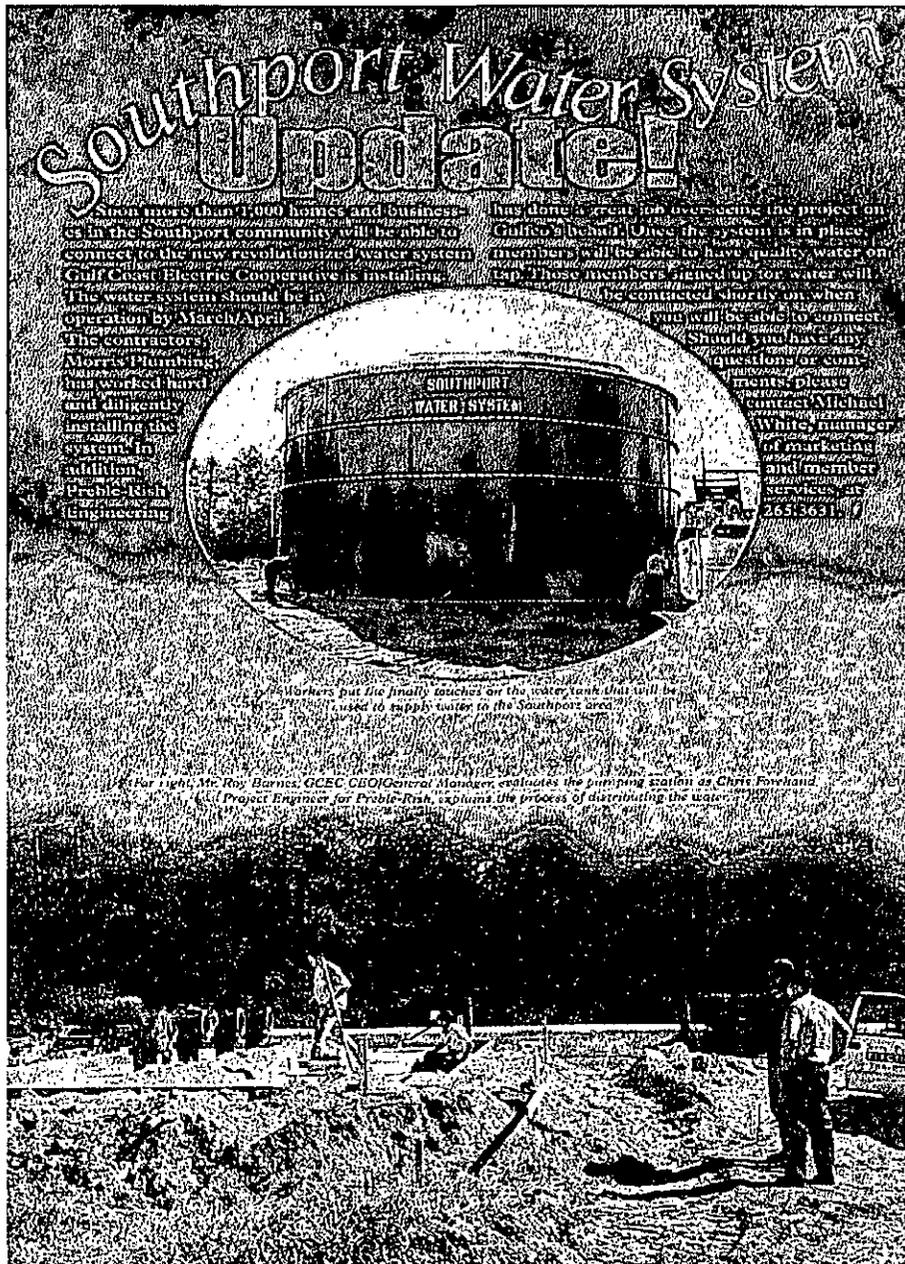


Article from Florida Living Magazine

SOUTHPORT WATER BOOSTER PLANT AND WATER SYSTEM

Client: Gulf Coast Electric Cooperative
 Reference: Mr. Michael White (850) 814-3778
 Location of Project: Southport, Florida
 Completion Date: 2008
 Brief Description:

Project consisted of a 341,000 gallon ground storage tank, four (4) 650 GPM high service pumps with variable frequency drives and over 60 miles of 4"-16" water mains. Firm's responsibility included the funding acquisition, project feasibility study, design, permitting and the construction administration of the project.

WATERSOUND NORTH - 30 MG GALLON REUSE RESERVOIR

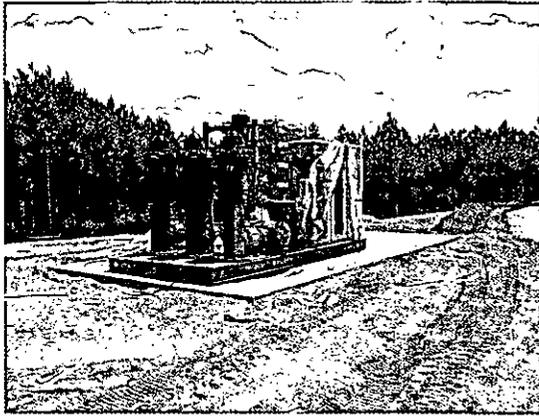

Client: The St. Joe Company
Reference: Ms. Mary Rosenheim (850) 231-6413
Location of Project: Walton County, Florida
Completion Date: 2006

Brief Description: This project involved the construction of a reuse reservoir to serve the irrigation needs of developments in southeast Walton County. This reservoir is a 30-million gallon earthen basin constructed above grade and lined with light-reflective 60-mil high density polyethylene (HDPE) liner. This reservoir receives public-access quality effluent from the Sandestin WWTP, Seacrest WWTP, and Point Washington WWTP. PRI was responsible for all surveying, engineering, permitting, and construction administration aspects of the project. PRI assisted in coordination between Regional Utilities and St. Joe Company to complete this project.

C. WILLINGNESS TO MEET SCHEDULE AND BUDGET REQUIREMENTS

Our team understands the importance of a complete and realistic project schedule. Upon receipt of a Notice to Proceed, our project team will take steps to ensure that project startup is a success and that it carries through to the end of the project schedule. Team members have an understanding of their roles and responsibilities as well as how their efforts are interrelated and have an effect on the rest of the project team. Open communication with the client and regulatory entities is paramount in maintaining a project schedule and budget.

D. EFFECT OF FIRM'S RECENT, CURRENT AND PROJECTED WORKLOAD

Over the past 5 years, PRI only lost 25% of its workforce due to the economy. Other firms reduced their size by 50% or more and some even closed their business. We feel that this demonstrates our strength in service to our current government clients. Our current workload is such that Preble-Rish, Inc. will be able to provide prompt and professional services to Leon County. PRI currently has the necessary staff to support the County's needs in a prompt and efficient manner.

E. EFFECT OF PROJECT TEAM LOCATION

Any utility engineering project that PRI will perform for Leon County will be handled out of our Crawfordville office and managed by Mr. Alan Wise. However, our wide-area network allows us to efficiently utilize the services of our professional staff from any office, on any job, while managing the project from its nearest and most logical location.

F. APPROACH TO THE PROJECT

Our approach is to keep you informed and up to date on project issues, communications and agency meetings. We will do so in a way that does not impose undue burden on the County. We will handle our responsibilities in an independent and professional manner while making sure that all decisions relating to the utility engineering projects are in keeping with the intentions of the scope of work as well as the desire of the County and its residents.
